




High School - April 2018



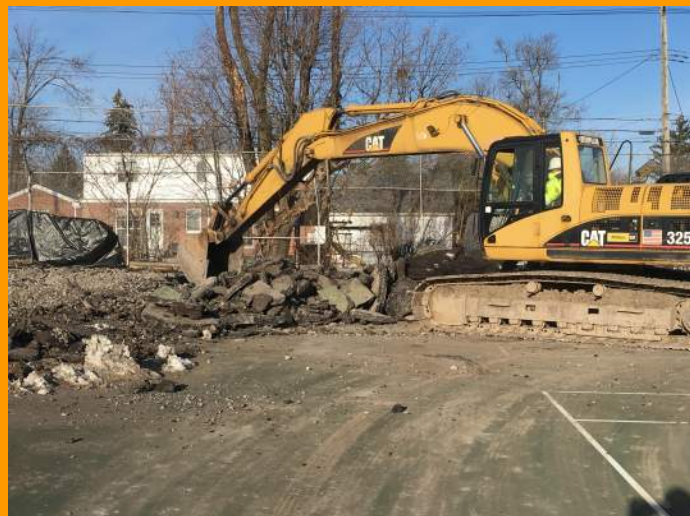

Amherst Central School District Capital Improvement Project



Summary Report No. 2 - April 2018

File 00585

Construction and Administrative Activities

I. Schedule:

Phase I High School Project:

HS Site Construction

Fall/Spring Construction is currently on schedule. Began on 3-5-18
Summer Construction is on schedule to begin on 5-25-18
Track and Field will be closed to Public on 5-25-18
Substantial Completion 9-7-18

HS ADA Lift Replacement

Summer Construction is on schedule to begin on 6-27-18
Substantial Completion is 7-31-18

Completed Activities:

Mobilization - Delivery of Equipment
Tennis Court Area: Demolition of existing fencing along HS Staff Parking Lot North West Corner
HS Track and Field Area: Installation of post driven temporary perimeter construction fencing and gates
HS Track and Field Area: Installation of mobile temporary perimeter construction fencing and gates
Tennis Court Area: Installation of Site protection
Tennis Court Area: Demolition of existing Tennis Court fencing
Utilities Survey and Markings / Ground Penetrating Radar
Tennis Court Area: Demolition of existing Tennis Court asphalt and accessories
Tennis Court Area: Demolition of Tennis Courts Asphalt access drives
Tennis Court Area: Site Survey and Layout for new grades
Tennis Court Area: Excavation and Sub grade work at Courts #1 and #2
New Shot Put/Discus Area: Excavation, Sub grade and Trench Drain work
New Shot Put/Discus Area: Installation of new drain inlets and storm lines

Current Activities:

Tennis Court Area: Installation of geotech fabric and 1st lift of 8" stone and compaction @ Court #1
Tennis Court Area: Installation of geotech fabric and 1st lift of 8" stone and compaction @ Court #2
Tennis Court Area: Excavation and Sub grade work at Courts #3 and #4
Tennis Court Area: Installation of geotech fabric and 1st lift of 8" stone and compaction @ Court #3
Tennis Court Area: Undercutting and structural sub base work Court #3 and #4
Tennis Court Area: Removal or excavated spoils and haul off site
New Shot Put/Discus Area: Installation of geotech fabric and stone sub base

Design/Engineering/Submittals:

Phase I High School:

Request for Information: Total of 9 RFI's have been processed and coordinated in the field
Project Submittals: 62% complete: Total of 208 submittals have been received and 139 have been processed
Coordination and monitoring of long lead time materials with the Prime Contractors

Next 30-days:

Tennis Court Area: Complete final stone sub base lift and compaction @ Courts #1 thru #4
Tennis Court Area: Excavation and Sub grade work at Court #5
Tennis Court Area: Installation of New Discus Cage foundation and footers
Tennis Court Area: Demolition of existing Discus/Shot put area
Removal of temporary site fencing at Track and Field
Tennis Court Area: Installation of New Discus Cage concrete pads
Tennis Court Area: Final grading at New Discus and Shot Put areas
Track and Field: Camera/Jetting/Vacuum of existing drain lines
Mobilize Track and Field work

Next 3 Months:

Tennis Court Area: Installation of Asphalt and Court surface/stripping
Tennis Court Area: Fencing, Gates and Accessories
Track and Field: Demolition of Track and Turf Field
Track and Field: Installation new Track surface and Turf Field replacement
Track and Field: Installation of new asphalt drives, walks and hardscapes

II. Safety:

No incidents to report to date.

Overall Project

III. Important Issues/Concerns:

No issues or concerns at this time



Exhibit A - Milestone Schedule

Amherst CSD Capital Improvement Project - Phase 1 Milestone Schedule

Run Date: 21-Dec-17 09:30

Activity ID	Activity Name	Start	Finish	Original Duration
Amherst CSD Capital Project - Phase 1				
BA1000	Bids Date	06-Feb-18	27-Feb-18	14
BA1010	School Board Approval/Notice To Proceed	06-Feb-18	06-Feb-18	0
BA1020	Contract Award	13-Feb-18	27-Feb-18	0
BA1030	Contractor Project Deliverables	13-Feb-18	27-Feb-18	10
Tennis Courts				
TC1000	Mobilization	05-Mar-18	20-Jul-18	98
TC1010	Install Temporary Fencing/ Site Protection	06-Mar-18	06-Mar-18	1
TC1020	Tennis Court Site Demolition	13-Mar-18	13-Mar-18	5
TC1030	Set Trench Drains	03-Apr-18	17-Apr-18	15
TC1040	Prep and Install Foundations and Footings	17-Apr-18	01-May-18	10
TC1050	Fill, Grade and Seed new Discus Area	01-May-18	15-May-18	10
TC1100	Concrete Paving @ New Discus and Shot Put Area	15-May-18	22-May-18	5
TC1060	Demolition of Asphalt Walk and Existing Discus and Shot Put	25-May-18	01-Jun-18	5
TC1070	Prep and Install Foundations and Footings - New Tennis Court	04-Jun-18	15-Jun-18	10
TC1120	Excavate and Install Gate Electrical Line	04-Jun-18	08-Jun-18	5
TC1080	Install Subgrade and Compact all Courts	18-Jun-18	22-Jun-18	5
TC1090	Asphalt Paving All Tennis Courts and Walkway	25-Jun-18	29-Jun-18	5
TC1100	Asphalt Cure Time - Tennis Courts	30-Jun-18	13-Jul-18	14
TC1130	Install Fence and Gates - Tennis Courts	02-Jul-18	16-Jul-18	10
TC1140	Tennis Court Surfacing and Striping	16-Jul-18	20-Jul-18	5
Track and Field				
TF1070	Camera/Jetting/Vacuum of Existing Drains and Storm Lines	06-Mar-18	13-Mar-18	5
TF1090	Last Day of Spring Sports	24-May-18	24-May-18	0
TF1080	Mobilize for Track and Field Installation	25-May-18	25-May-18	1
TF1100	Track and Field Site Demolition	29-May-18	18-Jun-18	15
TF1050	Track and Field Final Submittal/Approval/Material Release	04-Jun-18	04-Jun-18	0
TF1060	Turf Field Procurement	05-Jun-18	10-Jul-18	25
TF1110	Track and Field Foundations & Final Grading	12-Jun-18	25-Jun-18	10
TF1130	Asphalt Paving @ Track and Field	26-Jun-18	10-Jul-18	10
TF1140	Asphalt Cure Time	11-Jul-18	09-Aug-18	30
TF1150	Turf Field Installation	11-Jul-18	07-Aug-18	20
TF1160	Install Fence and Site Features	11-Jul-18	31-Jul-18	15
TF1180	Landscape Restoration	01-Aug-18	14-Aug-18	10
TF1170	Track Surfacing and Striping	10-Aug-18	23-Aug-18	10
TF1270	Track Surfacing Cure Time	24-Aug-18	30-Aug-18	5
High School ADA Lifts				
ADA1250	ADA Lift Mobilization	25-Jun-18	31-Jul-18	28
ADA1220	Multipurpose Room ADA Lift Replacement	25-Jun-18	25-Jun-18	1
ADA1230	Auditorium ADA Lift Replacement	26-Jun-18	24-Jul-18	20
ADA1240	ADA Lift Testing and Certification	25-Jul-18	31-Jul-18	20
Completion Activities				
CA1260	Substantial Completion ADA Lifts	31-Jul-18	14-Sep-18	32
CA1200	Site Punchlist Issued	31-Jul-18	31-Jul-18	0
CA1210	Punchlist Completion	24-Aug-18	23-Aug-18	0
CA1190	Substantial Completion - Tennis Track and Field	07-Sep-18	07-Sep-18	10
CA1220	Owner FF&E	14-Sep-18	14-Sep-18	0
CA1230	First Home Football Game	14-Sep-18	14-Sep-18	5

4-27-18; Data Line

